




NOTES:
1.DO NOT SCALE FROM THIS DRAWING.
2.ALL DIMENSIONS MUST BE CHECKED/VERIFIED ON SITE.
3.UNLESS OTHERWISE STATED ALL DIMENSIONS IN MILLIMETERS.
4.TENDER DRAWINGS ARE CONSIDERED INDICATIVE & SUBJECT TO CHANGES FOR COSTING PURPOSES UNTIL DESIGN DRAWING ARE ISSUED.

REVISIONS			
REV	DATE	DETAILS OF DESCRIPTION	CHK'D

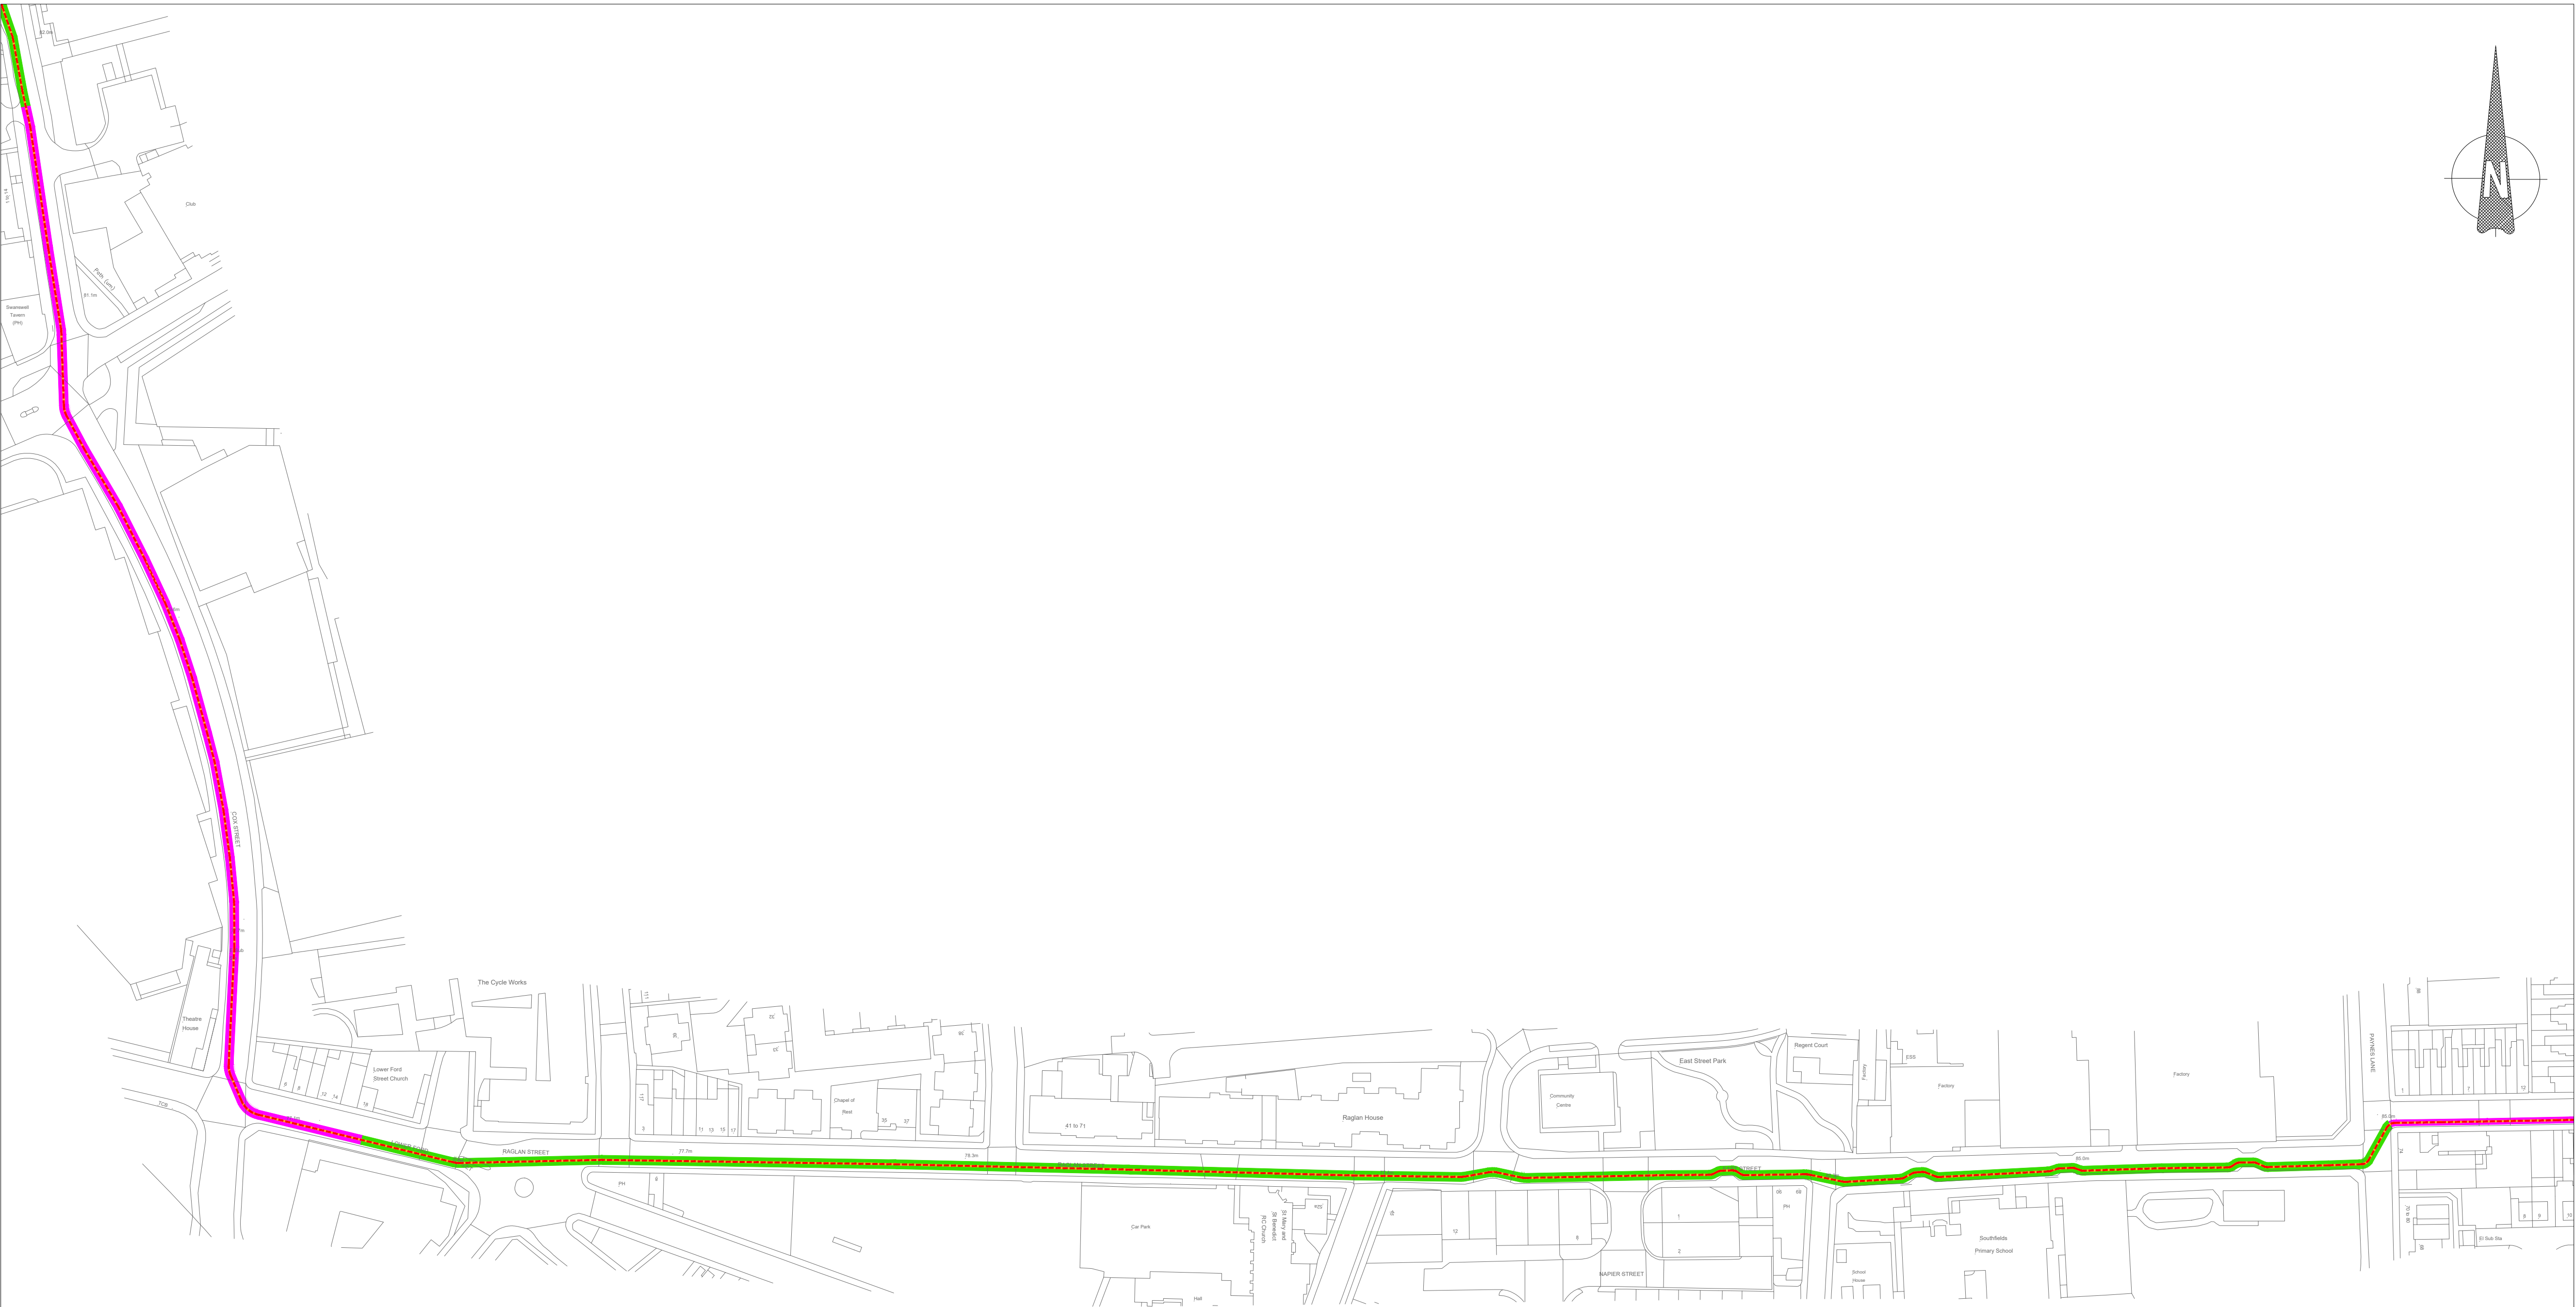

Matrix Networks

Head Office
Eleanor House
Newport Pagnell
Road West
Northampton
NN4 7JJ
Tel: 01604 654 282

Northern Office
6500 Daresbury Park
Daresbury
Warrington
WA4 4GE
Tel: 0844 74 000 74
Fax: 0844 74 000 75

Southern Office
7 Lidstone Court
George Green
Slough
SL3 6AW
Tel: 01753 578 971




UK Power Distribution

Head Office
Eleanor House
Newport Pagnell
Road West
Northampton
NN4 7JJ
Tel: 01604 654 282

Northern Office
6500 Daresbury Park
Daresbury
Warrington
WA4 4GE
Tel: 0844 74 000 74
Fax: 0844 74 000 75

Southern Office
7 Lidstone Court
George Green
Slough
SL3 6AW
Tel: 01753 578 971

EXCAVATED DUCT INSTALLED AND REINSTATED	
EXCAVATED AND PART DUCTED	
EXCAVATION WORKS FOR FOLLOWING WEEK	

PROJECT TIMELINE	WEEK COMMENCING 10TH AUGUST 2026	WEEK COMMENCING 17TH AUGUST 2026	WEEK COMMENCING 24TH AUGUST 2026	WEEK COMMENCING 31TH AUGUST 2026	WEEK COMMENCING 7TH SEPTEMBER 2026
	WEEK 1	WEEK 2	WEEK 3		
EXPECTED EXCAVATION LENGTH PER WEEK	150m	150m	150m	150m	150m
ACTUAL EXCAVATION LENGTH PER WEEK	150m	150m	150m	150m	150m
